



Walkable Chadds Ford

Chadds Ford Township, Delaware County, PA

October 7, 2020 - Board of Supervisors Meeting


The Goals for the Walkable Chadds Ford Project are to:

- Enhance Pedestrian, Cyclist and Motorist Safety
- Calm Traffic
- Create non-vehicular connections between destinations
- Extend the length of visits to the Village area
- Enhance the aesthetic character of the Village
- Foster Economic Development
- This planning and design process was initiated in 2016 by the Township and the Brandywine Conservancy.


TA Set-Aside Application



CITY/TOWN	COUNTY	ROUTE	SECTION	SHEET
ELM HURST	ELM HURST	SR 3101	W/F	15 OF 25
ELM HURST	ELM HURST	SR 3101	W/F	15 OF 25
(HARRIS FORD AND HENNSBURY TOWNSHIP)				
REVISION NUMBER	REVISIONS	BY	DATE	

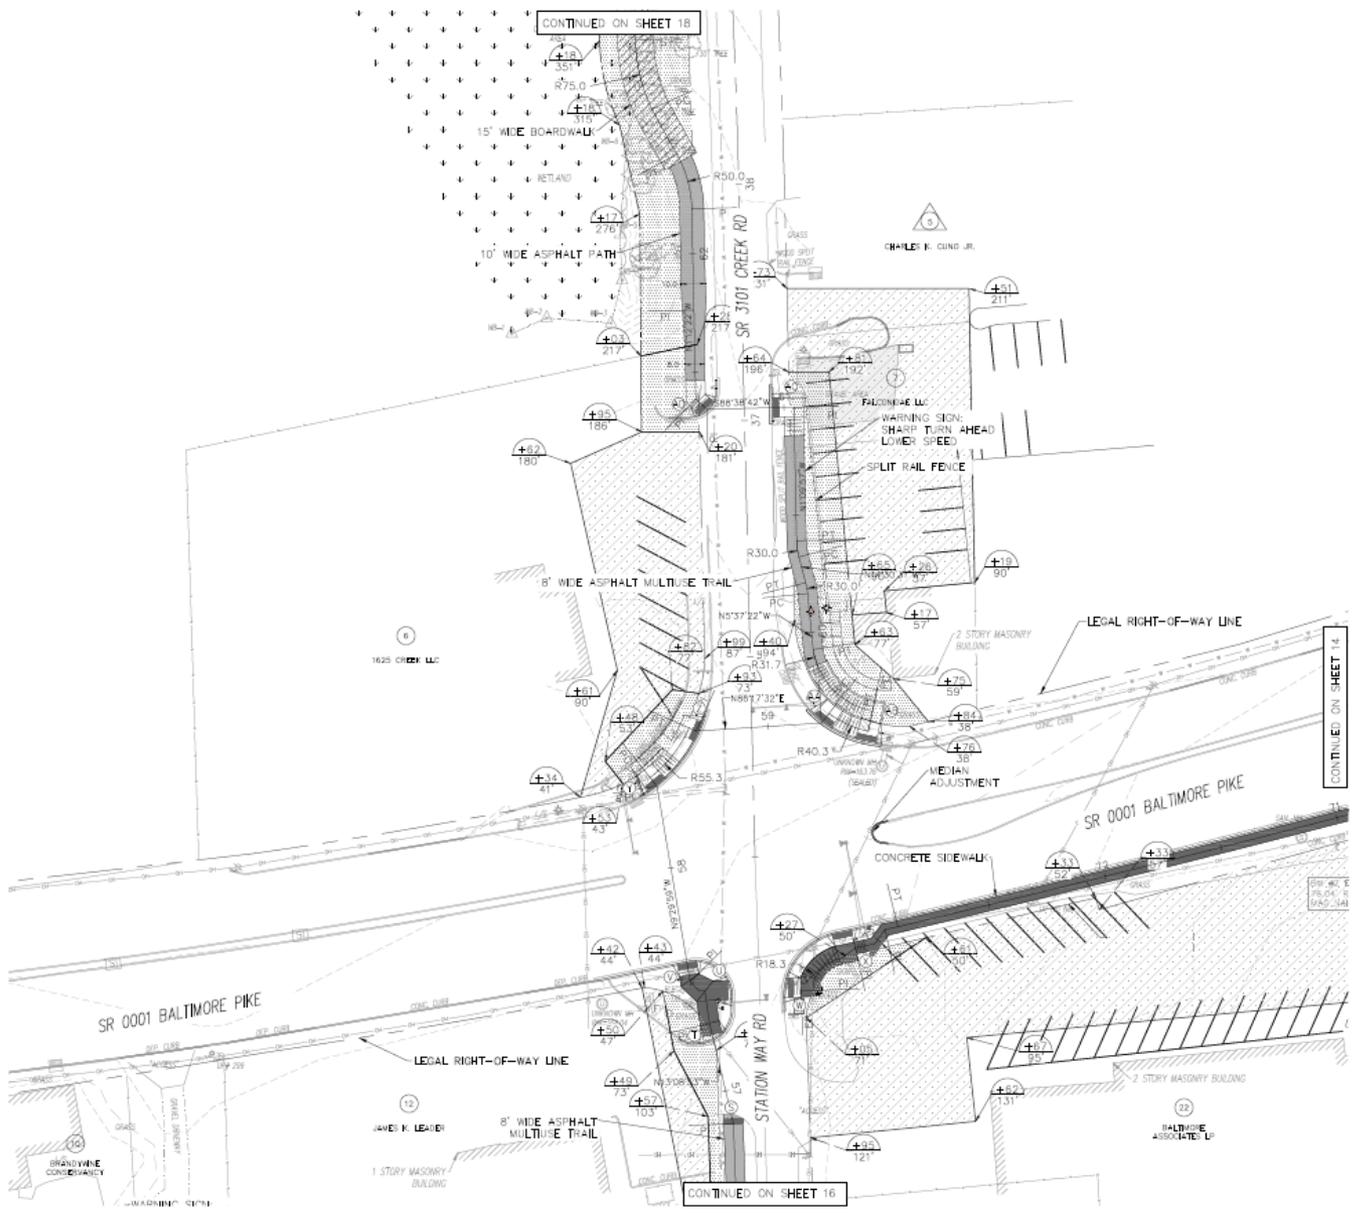

- LEGEND:**
- PROPOSED VEGETATION PATH
 - PROPOSED BOARDWALK
 - PROPOSED GRAVEL PATH
 - PROPOSED CURB RAMP (REFER TO ADA PLAN)
 - LEGAL SIGNAGE EXISTENT
 - TEMPORARY CONSTRUCTION EXISTENT
 - EXISTING WETLAND







FOR PROFILE SEE SHEET 24-25



Chadds Ford Village

DISTRICT	COUNTY	ROUTE	SECTION	SHEET
ABINGTON TOWNSHIP				
REVISION NUMBER	REVISIONS	DATE	BY	

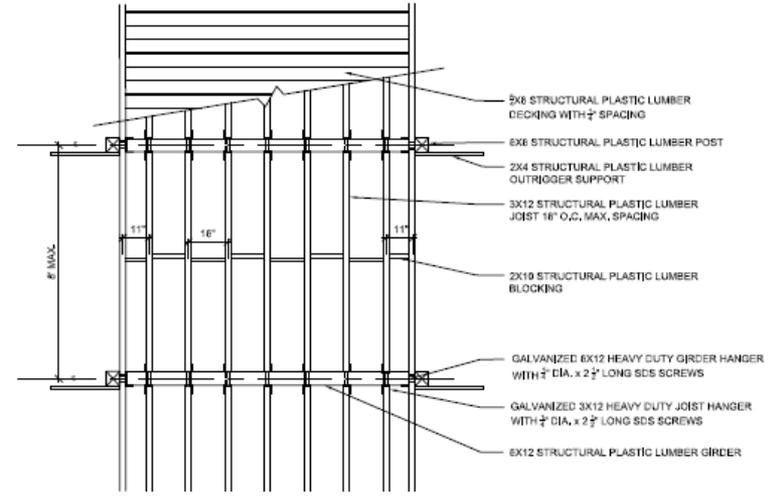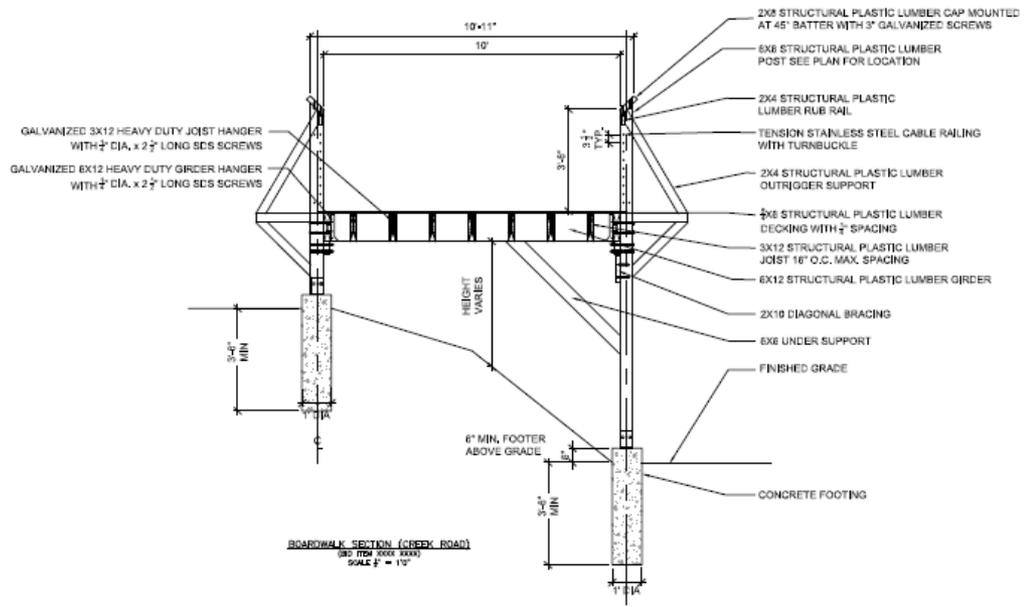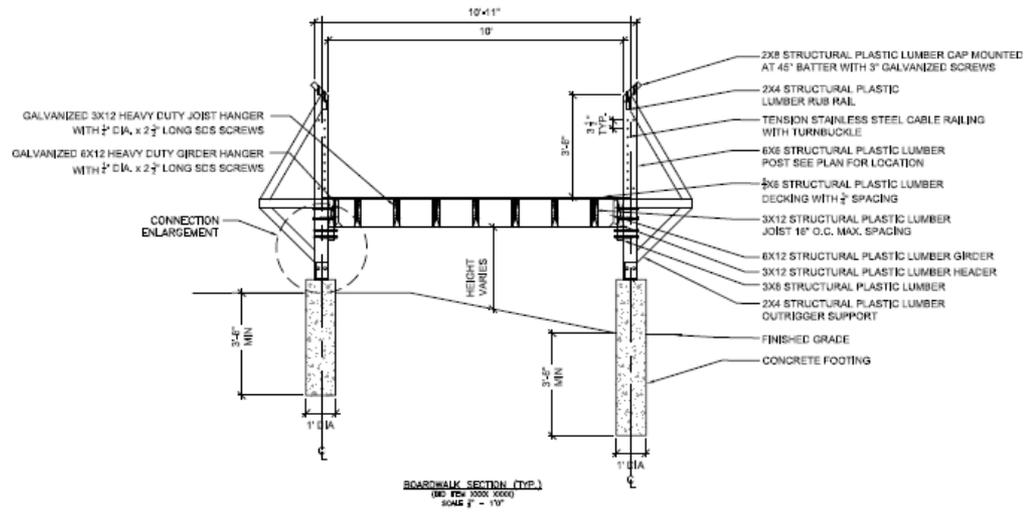

Project Schedule Summary

- Final re-submissions of staged plans to PennDOT / DVRPC over the next 30+ days.
- PS&E submission (final approvals) anticipated in Jan / Feb 2021.
- Final PennDOT approval anticipated March 2021.
- Bidding anticipated in spring 2021
- Phase 1 construction summer 2021

Walkable Chadds Ford – Project Status – Remaining Schedule as of 10/7/2020

Plan Submission / PennDOT Reviews & Approvals

ADA, submitted: June 18, 2010, Comments Received: August 28, 2020.

- Kimley Horn is currently coordinating with Joe Natale to confirm if the ADA revisions can be handled via design-build. Drafting changes to the ADA placement per the comments from PennDOT will still be required.
- Assuming the ADA design aspect of the review can be design-build, the full resubmission to PennDOT can occur by end of October.
- If PennDOT requires full ADA design to be included, then the resubmittal will be submitted by 11/13

Traffic Signals: Submitted June 18, 2020, Comments Received: July 29, 2020. Minor comments to be incorporated in PS&E submission.

Traffic Operations: Submitted June 18th, 2020, Comments Received: Sept 24, 2020. Minor comments to be incorporated in PS&E submission.

ROW Plans. Kimley Horn is coordinating with Joe Natale now to submit right of plans for PennDOT review. Assume a formal submission by 10/16, if Joe has any comments or feedback. Once these plans are approved by PennDOT, the Township can begin negotiation for easements with property owners.

Simone Collins is completing structural design of boardwalk. This will be submitted to Township (engineer) for independent third-party review.

Submit PS&E Package following PennDOT approval (1st quarter 2021)

Walkable Chadds Ford – Project Status – Remaining Schedule as of 10/7/2020

Permitting / Environmental / Historic – Cultural

Cultural Resources:

Revised Archeology Phase 1 Submitted to PennDOT (9/1/2020), approval pending (~30days)

Historic Resources Effects Memo – Submission to PennDOT (9/23/2020), PennDOT approval/Posting (~30days), PHMC approval (30days) – 12/15/2020

Public Involvement: Tonight's meeting with the Board of Supervisors is a part of the required public involvement process.

Section 4f evaluation: When the cultural resources Finding is approved by PHMC, Sec 4(f) can be submitted for PennDOT/FHWA approval (12/15/2020 submission, 01/15/2021 approval)

CEE: submission 01/15/2021, 02/15/2021 approval)

Permit: General Permit 7, Need preliminary plans to determine aquatic impact, construction drawings, cross-sections of impacts. Anticipate submittal to DEP week of Oct 19th (approval in 55 days).

Walkable Chadds Ford – Project Status – Remaining Schedule as of 10/7/2020

Utility Clearances

Utility Clearances received From:

- CFT Sewer Authority
- Chester County Water Authority
- Crown Castle
- Columbia Gas
- Comcast Cable/ Fiber
- Verizon

Utility Clearances pending from

- PECO (Called Thurs 10.1.20)
- TC Energy (Called Thurs 10.1.20)

Walkable Chadds Ford



Thank you for your time

Questions, comments, discussion
